

**BOUW**

**INFRA**

**RENOVATIE-  
TECHNIEKEN**

**VASTGOED**

**TUNNELLING**

**PPP**

**K KUMPEN**

# Nieuw kantoor Kumpen NV




Nieuwbouw kantoor Kumpen – arch. Stramien, ir. stab. Establis, ir. tech. Sweco

$$E=mc^2$$

Groene tijd – rode tijd




5+13, of 13+5

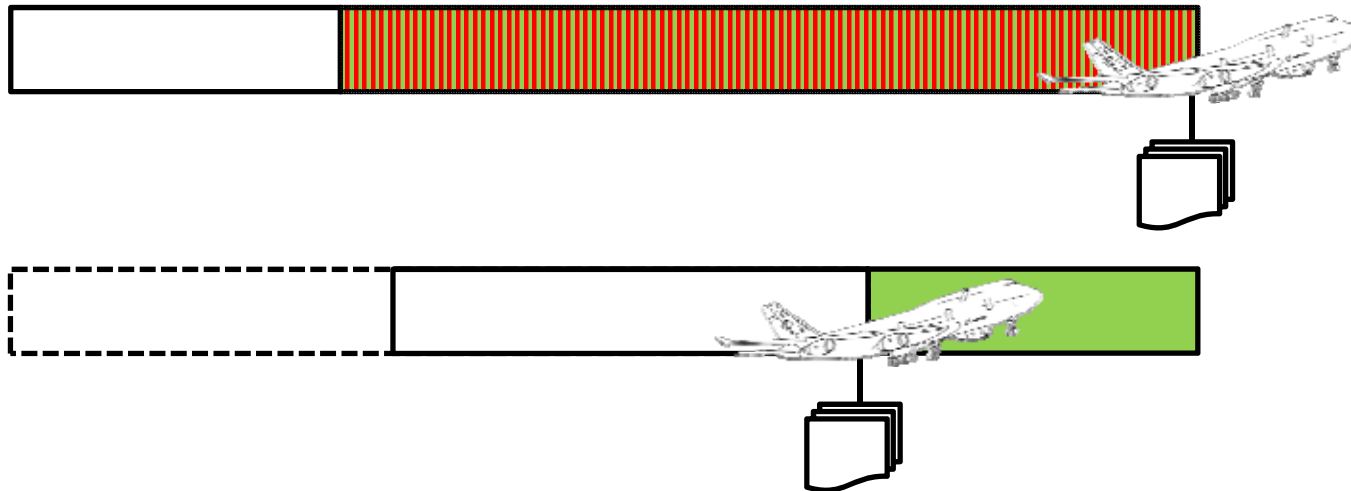




BIM

LOD

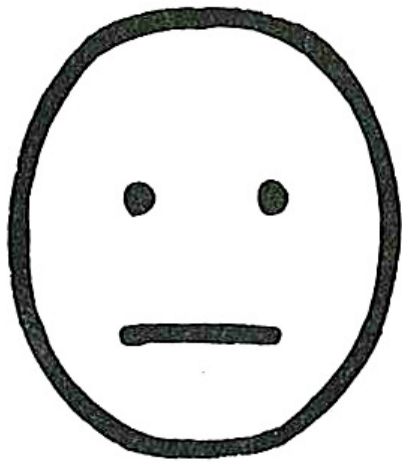

100



200



300



400



LOD


 **KUMPEN**





# Clashcontrole

**KUMPEN**

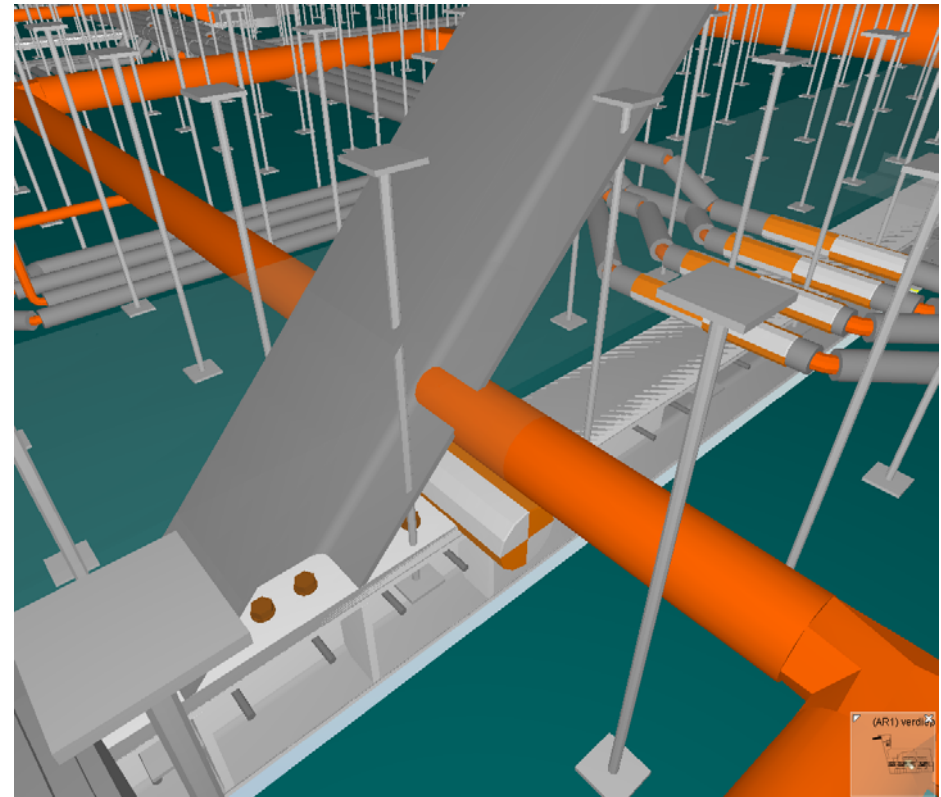


# Communicatie

## Stadskantoor Hasselt

[Settings](#) Project leader



Project owner: Dieter Froyen  
 Start date: 27-03-2017  
 End date: -



Issues: 241  
 Team members: 15  
 Pending: 6

241	+2 Poolje verplaatsen	Closed off-lin...	Lise Bibert	Comment added by lbi 31-05-2017 14:05	Closed	31-05-2017
240	+2 Bakje in betonbalk getekend	Updated off-l...	Lise Bibert	Comment added by lbi 31-05-2017 13:57	Active	31-05-2017
239	+3 Overbruggen	Updated off-l...	Lise Bibert	Comment added by lbi 31-05-2017 13:38	Active	31-05-2017
238	+3 Overbruggen	Updated off-l...	Lise Bibert	Comment added by lbi 31-05-2017 13:38	Active	31-05-2017
237	+3 Overbruggen?	Updated off-l...	Lise Bibert	Comment added by lbi 31-05-2017 13:38	Active	31-05-2017
236	+3 Overbruggen?	Updated off-l...	Lise Bibert	Comment added by lbi 31-05-2017 13:37	Active	31-05-2017
235	+3 Overbruggen	Updated off-l...	Lise Bibert	Comment added by lbi 31-05-2017 13:37	Active	31-05-2017
234	+3 Overbruggen	Updated off-l...	Lise Bibert	Comment added by lbi 31-05-2017 13:36	Active	31-05-2017
233	+3 Overbruggen	Updated off-l...	Lise Bibert	Comment added by lbi 31-05-2017 13:35	Active	31-05-2017
232	+3 Overbruggen?	Updated off-l...	Lise Bibert	Comment added by lbi 31-05-2017 13:34	Active	31-05-2017


[Go to activities](#)

## Kuborn (Citygate)

[Settings](#) Project leader



Project owner: Sien van der Have  
 Start date: 09-01-2017  
 End date: 29-07-2019



Issues: 447  
 Team members: 19

414	SDB changée? Position bagno...	Resolved	Sebastien Baud...	New comment added.	Resolved	13-06-2017
444	Add schedules to your model (...)	Resolved	Sebastien Baud...		Resolved	13-06-2017
447	Can you add the schedule 'KU...	Resolved	Sebastien Baud...		Resolved	13-06-2017
338	Nouveau schedule à Chapoo	Resolved	Sebastien Baud...		Resolved	13-06-2017
305	Positions machine à laver	Resolved	Sebastien Baud...		Resolved	13-06-2017
303	App block B dans le coin	Resolved	Sebastien Baud...		Resolved	13-06-2017
283	Décalage de trémie dans la ch...	Resolved	Sebastien Baud...		Resolved	13-06-2017
447	Can you add the schedule 'KU...	Created	Sien van der H...	Title set to 'Can you add the schedule 'K...	Resolved	07-06-2017
446	Can you check your clashcontr...	Created	Sien van der H...	Title set to 'Can you check your clashcon...	Active	06-06-2017
445	Can you check your levels? l'v...	Created	Sien van der H...	Title set to 'Can you check your levels? l'...	Active	06-06-2017

[Go to activities](#)

VR



**K KUMPEN**



(ref. WATT – Stramien)

# 4D



The screenshot displays a software interface for 4D construction management. It features a Gantt chart at the top, a 3D model of a building foundation in the center, and a list of tasks on the right. The Gantt chart shows a timeline from January 2016 to January 2018, with various tasks represented by colored bars. The 3D model shows a grid of foundation elements with vertical columns representing construction progress. The task list on the right includes details such as ID, Name, Duration, Start, and Finish for various construction activities.

ID	Name	Duration	Start	Finish	Navwa
1	opstellen definitief ontwerp in BT	21d, 0h	8.30 21032015 (A)	10.30 31032015 (A)	LO--
2	opstellen vergunningaanvragen	26d, 5h	8.30 20032015 (A)	14.00 10042015 (A)	LO--
3	indiening vergunningaanvragen	0d		17.00 13042015 (A)	LO--
4	verlating ontkentelijkheid en volledigheid	21d	8.30 14042015 (A)	17.00 13052015 (A)	LO--
5	behandeling vergunningsdossier (adviesrapport)	47d, 7h	8.30 18052015 (A)	16.00 14082015 (A)	LO--
6	verlenen van vergunning	0d		17.00 30082015 (A)	LO--
7	aanvoorspelling	42d, 4h, 30m	8.30 4082015 (A)	13.30 31102015 (A)	LO--
8	stand still periode (beplanning en berepsm...)	20d, 23h, 59m	17.00 30082015 (A)	17.00 21102015 (A)	LO--
9	gunning van het project, stand-still en aanvangsb...	104d, 1h	8.30 51102015 (A)	8.30 16032016 (A)	LO--
10	start werken	0d	8.30 06052016 (A)		LO--
11	contractuele einddatum	0d	8.30 20072018		LO--
12	einddatum werfbudget	0d	8.30 06052016		LO--
13	werfsliding	10d	8.30 06052016 (A)	17.00 23052016 (A)	LO--
14	explosieonderzoek: uitzetten putten	0d	8.30 06052016 (A)		LO--
15	ontgraven bestaande drinkwaterleidingen	1d	8.30 10052016 (A)	17.00 10052016 (A)	LO--
16	explosieonderzoek: plaatselijke ontgravingen	13d	8.30 11052016 (A)	17.00 30052016 (A)	LO--
47	monitoren	10d	8.30 24052016 (A)	17.00 03062016 (A)	LA--

# 5D



Overzicht totale hoeveelheden per versie model.txt - Excel

BESTAND START INVOEGEN PAGINA-INDELING FORMULES GEGEVENS CONTROLLEREN BEELD GEO-IT C3A novaPDF van der Have...

Calibri 11 Standaard Voorwaardelijke opmaak Invoegen Opmaak als tabel Verwijderen Opmaak Bewerken


Klambord Lettertype Uitlijning Getal Celstijlen Cellen

A17 09.07.33 akoestische schotten 100

Artikel	Component	TI	EH	6/07/2016	12/08/2016	30/08/2016	14/09/2016	AR
13.01.41	Kitchenette met fronten uit HPL en corpus uit gr	Furniture	st	2	2 /			2
13.01.42	Kitchenette met fronten uit HPL en corpus uit gr	Furniture	st	6	6 /			6
13.01.43	Kitchenette met fronten uit HPL en corpus uit gr	Furniture	st	1	1 /			1
13.02.75	Wastablet sanitair-0.5	Furniture	st	2	2 /			2
13.02.76	Wastablet kantoren	Furniture	st	30	32 /			33
13.03.71	Lockers	Furniture	st	13	13 /			20
13.03.72	Lockers kantoorzone	Furniture	st		13 /			13
14.03.52	wand spiegel type 1	Furniture	st	32	32 /			33
14.03.53	Spiegel type 2	Furniture	st	2	2 /			2
09.07.32	Brandschotten 100	Wall	m	1182,75	1169,91 /			
09.07.32	Brandschotten - foute hoogte	Wall	94 m					30,79
09.07.32A	Brandschotten - 48cm	Wall	m			96,118		96,12
09.07.32C	Brandschotten - 74cm	Wall	m			1501,04		1478,18
09.07.32C'	Brandschotten - 74cm - Gebogen	Wall	95 m					28,22
09.07.33	akoestische schotten 100	Wall	m	59,17	1202,93	892,843		855,27
09.07.33'	akoestische schotten 100 - Gebogen	Wall	90 m					35,12
09.14.22	Stalen gemoffelde binnentrappandgreep muurb	Railing	70 m					
09.14.23	Stalen gemoffelde binnentrappandgreep / leuni	Railing	70 m					
09.14.24	Balustrade vide (Recht) 90 x 1170	Railing	88 m			/		
09.14.24	Balustrade vide (Recht) 90 x 1170	Wall	m					12,83
09.14.25	Balustrade vide (Gebogen) 90 x 1170	Railing	88 m			/		

GEREED

# Werkplannen




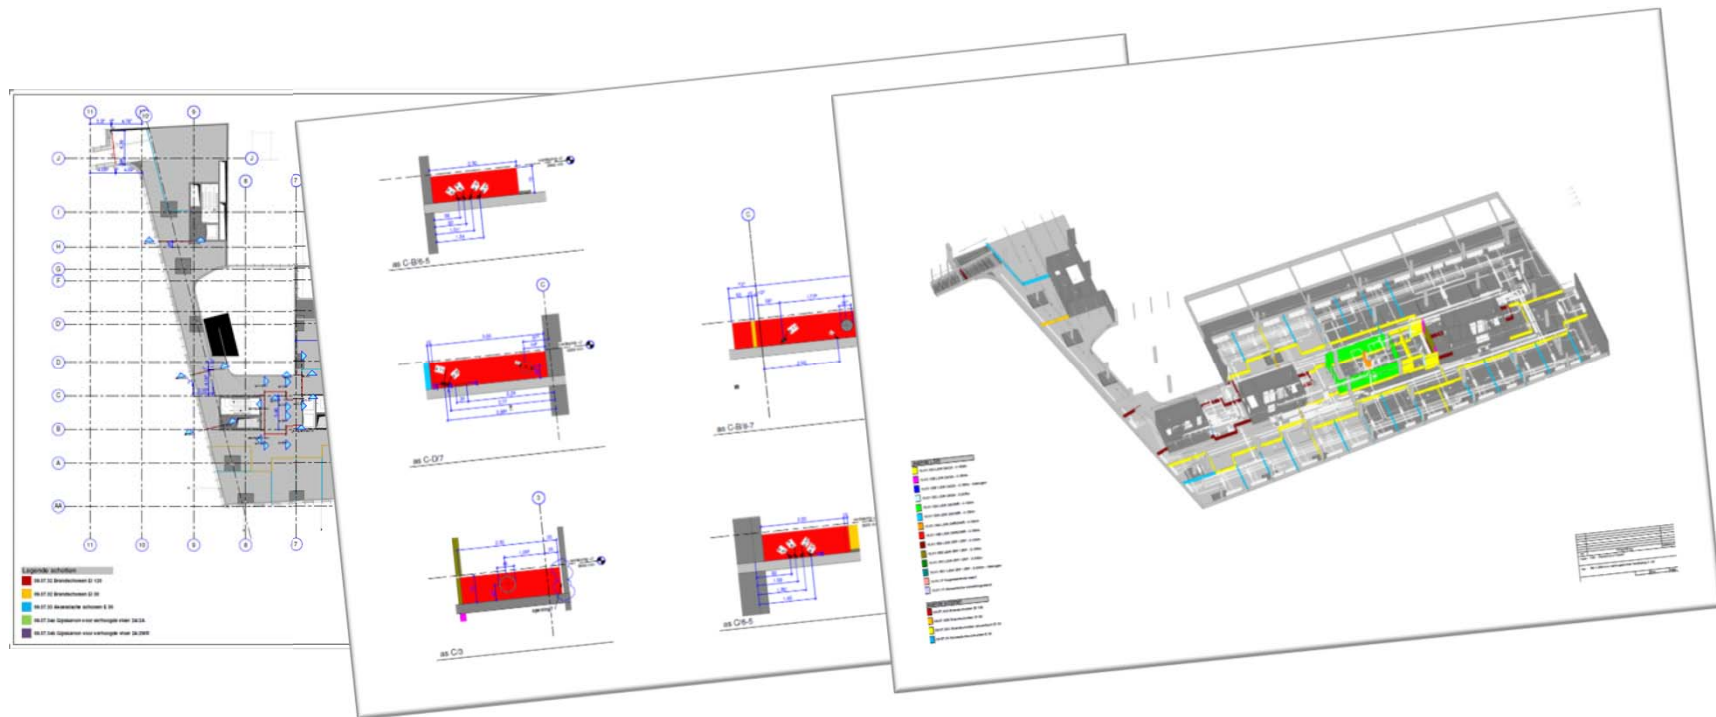


Lean

 **KUMPEN**




# Concurrent engineering

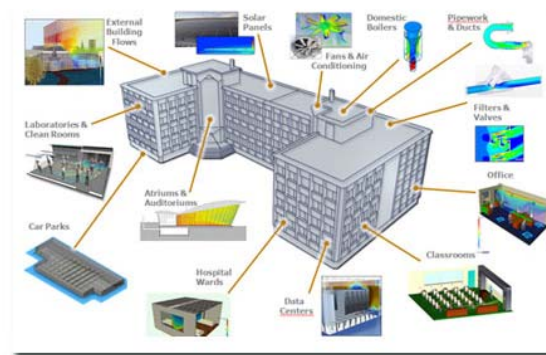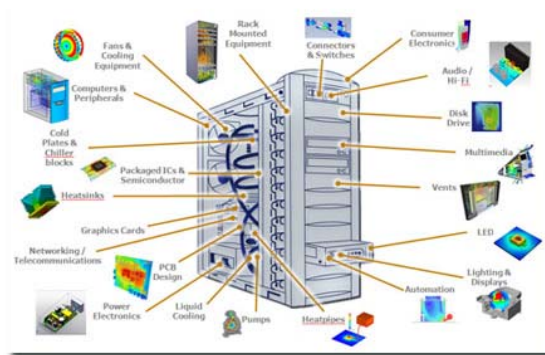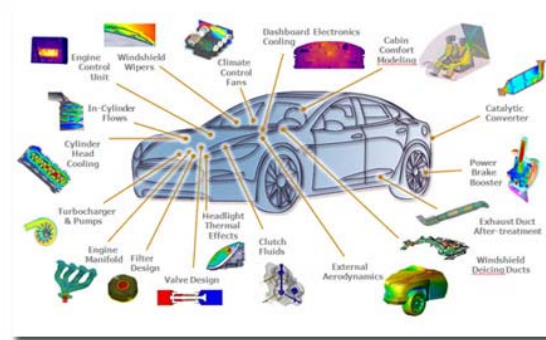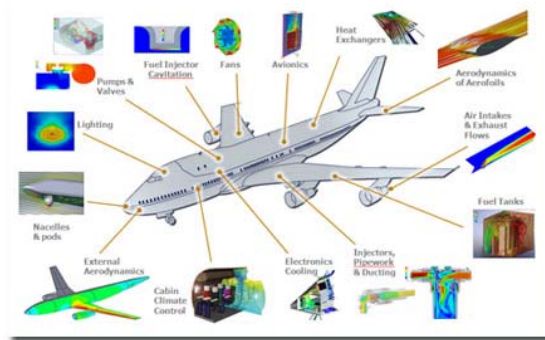



# Plakkertjesplanning

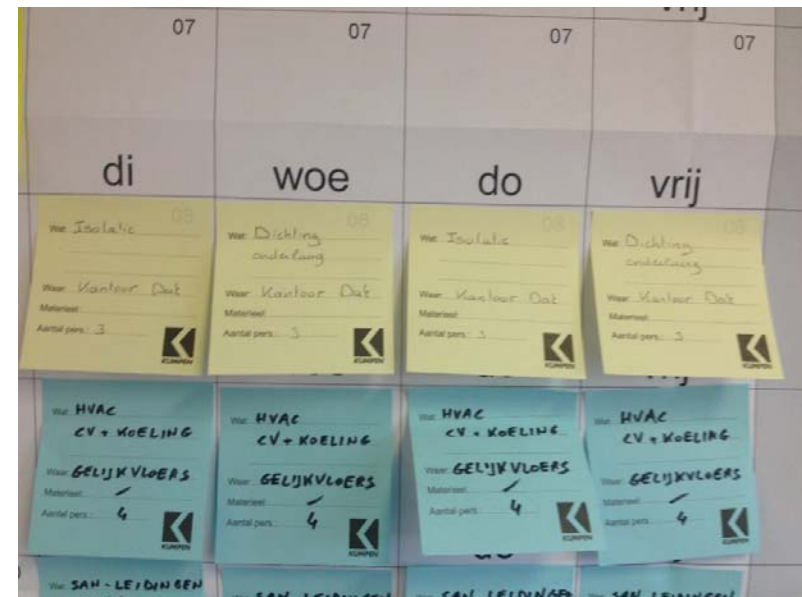



/2017
